
Cane Creek Greenway Extension
Town of Fletcher

ID	Task Name	Duration	Start	Finish	% Complete
1	**Cane Creek Greenway Ext**	**463 days**	**Fri 10/3/25**	**Tue 7/13/27**	**18%**
2	**Overall Greenway Extension Master Planning**	**27 days**	**Fri 10/3/25**	**Mon 11/10/25**	**100%**
3	Project Kickoff	1 day	Fri 10/3/25	Fri 10/3/25	100%
4	Site Visit/Evaluation	5 days	Mon 10/6/25	Fri 10/10/25	100%
5	Conceptual Base Map Creation	5 days	Wed 10/22/25	Tue 10/28/25	100%
6	Complete Cost Estimate	2 days	Wed 10/29/25	Thu 10/30/25	100%
7	Meet with Town of Fletcher to Re	1 day	Fri 10/31/25	Fri 10/31/25	100%
8	Update Concept & Cost Estimate as Needed	5 days	Mon 11/3/25	Fri 11/7/25	100%
9	Approval from Town of Fletcher to Proceed with Design	1 day	Mon 11/10/25	Mon 11/10/25	100%
10	**GTSP Environmental Review**	**76 days**	**Wed 10/8/25**	**Wed 1/21/26**	**67%**
11	Site Visit/Evaluation	10 days	Wed 10/8/25	Tue 10/21/25	100%
12	Complete Enironmental Review	5 days	Thu 1/15/26	Wed 1/21/26	0%
13	**Design, Permitting, and Construction Documents**	**282 days**	**Tue 11/11/25**	**Wed 12/9/26**	**19%**
14	Base Map Creation	15 days	Tue 11/11/25	Mon 12/1/25	100%
15	Complete Initial Design Drawings	32 days	Tue 12/2/25	Wed 1/14/26	100%
16	Obtain Easement from Charlie Owen and Fernleaf	185 days	Thu 1/15/26	Wed 9/30/26	0%
17	Prepare and submit NCDOT Encroachment/Driveway Permits	40 days	Thu 10/1/26	Wed 11/25/26	40%

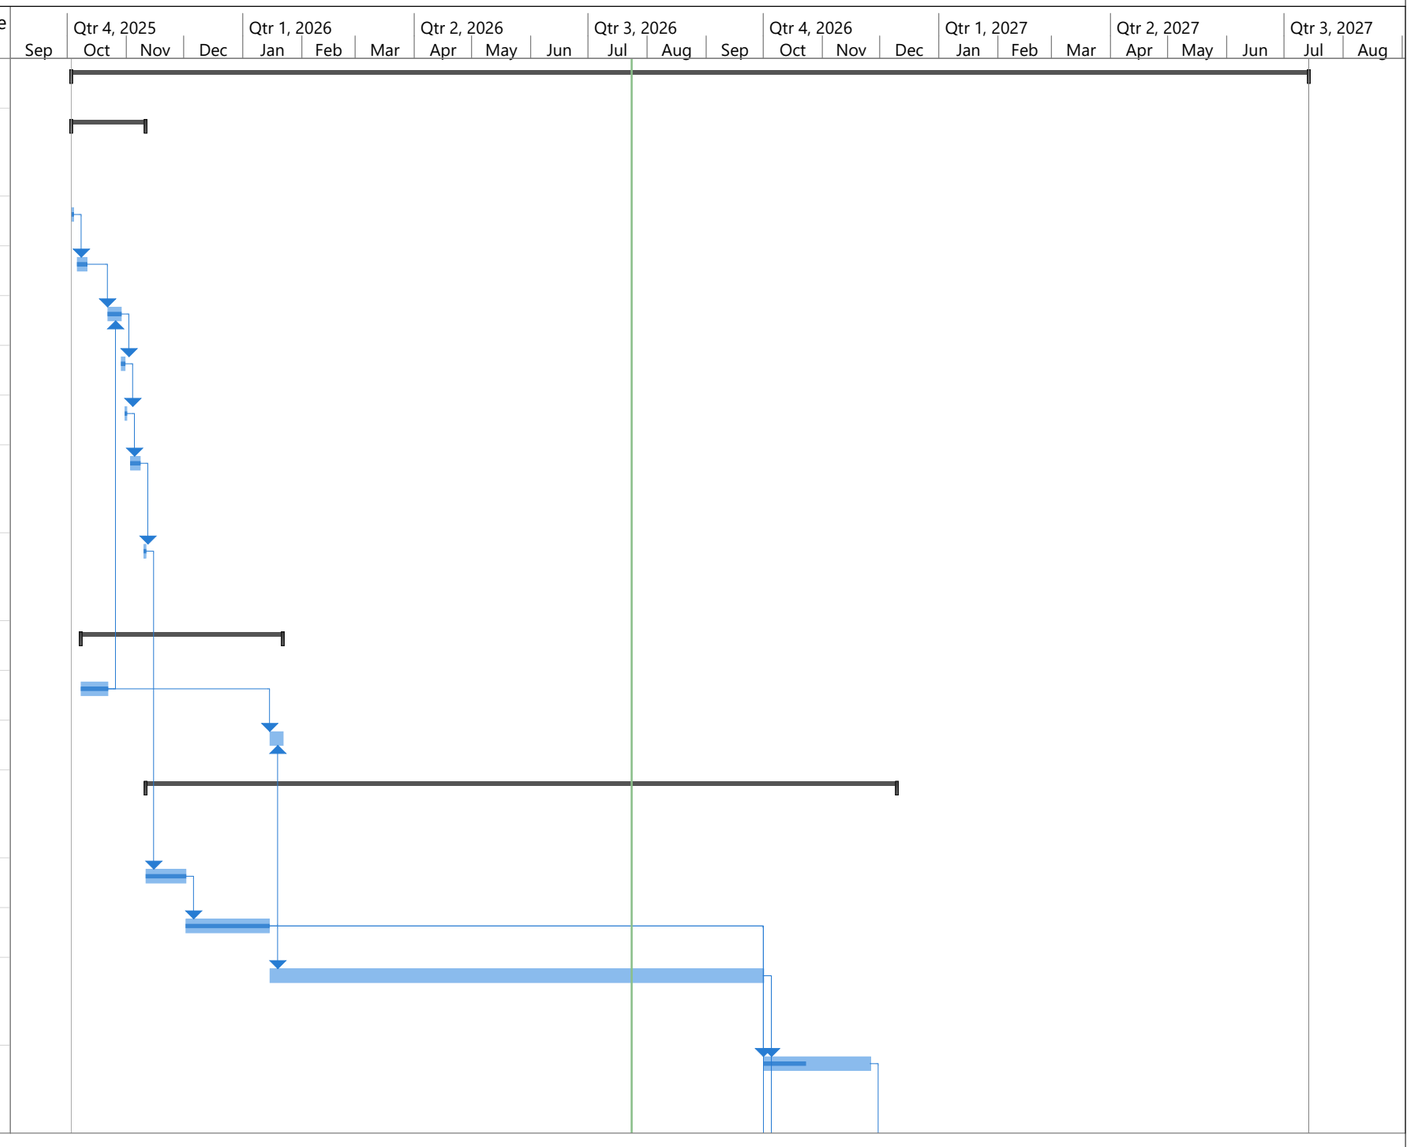


Project: 25.00136 FletcherNC-C
Date: Fri 7/24/26

Task	Project Summary	Manual Task	Start-only	Deadline
Split	Inactive Task	Duration-only	Finish-only	Progress
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress
Summary	Inactive Summary	Manual Summary	External Milestone

Cane Creek Greenway Extension
Town of Fletcher

ID	Task Name	Duration	Start	Finish	% Complete
18	Prepare and Submit "No Rise" Certification to Town of Fletcher	15 days	Thu 10/1/26	Wed 10/21/26	0%
19	Prepare Erosion Control Permit Package and Submit to NCDEQ	40 days	Thu 10/1/26	Wed 11/25/26	20%
20	Submit Environmental Review Package for approval	40 days	Thu 10/1/26	Wed 11/25/26	0%
21	Revise Permit Drawings as necess	10 days	Thu 11/26/26	Wed 12/9/26	0%
22	**Bidding & Award**	**68 days**	**Thu 12/10/26**	**Mon 3/15/27**	**0%**
23	Compile Bid Set & Advertise	10 days	Thu 12/10/26	Wed 12/23/26	0%
24	Conduct Pre-Bid Meeting	1 day	Thu 12/24/26	Thu 12/24/26	0%
25	Bidding/Complete Addenda as necessary	25 days	Fri 12/25/26	Thu 1/28/27	0%
26	Conduct Bid Opening Meeting	1 day	Fri 1/29/27	Fri 1/29/27	0%
27	Evaluate Bid Results and Prepare Recommendation of Award	15 days	Mon 2/1/27	Fri 2/19/27	0%
28	Attend Council Meeting for Final Approval	1 day	Mon 2/22/27	Mon 2/22/27	0%
29	Prepare Conformed Drawings and Execute Notice to Proceed	15 days	Tue 2/23/27	Mon 3/15/27	0%
30	**Construction Administration/Observation**	**86 days**	**Tue 3/16/27**	**Tue 7/13/27**	**0%**
31	Attend Pre-Construction Meeting	1 day	Tue 3/16/27	Tue 3/16/27	0%
32	Construction	65 days	Wed 3/17/27	Tue 6/15/27	0%
33	Project Closeout	20 days	Wed 6/16/27	Tue 7/13/27	0%
34	**Project Complete**	**0 days**	**Tue 7/13/27**	**Tue 7/13/27**	**0%**

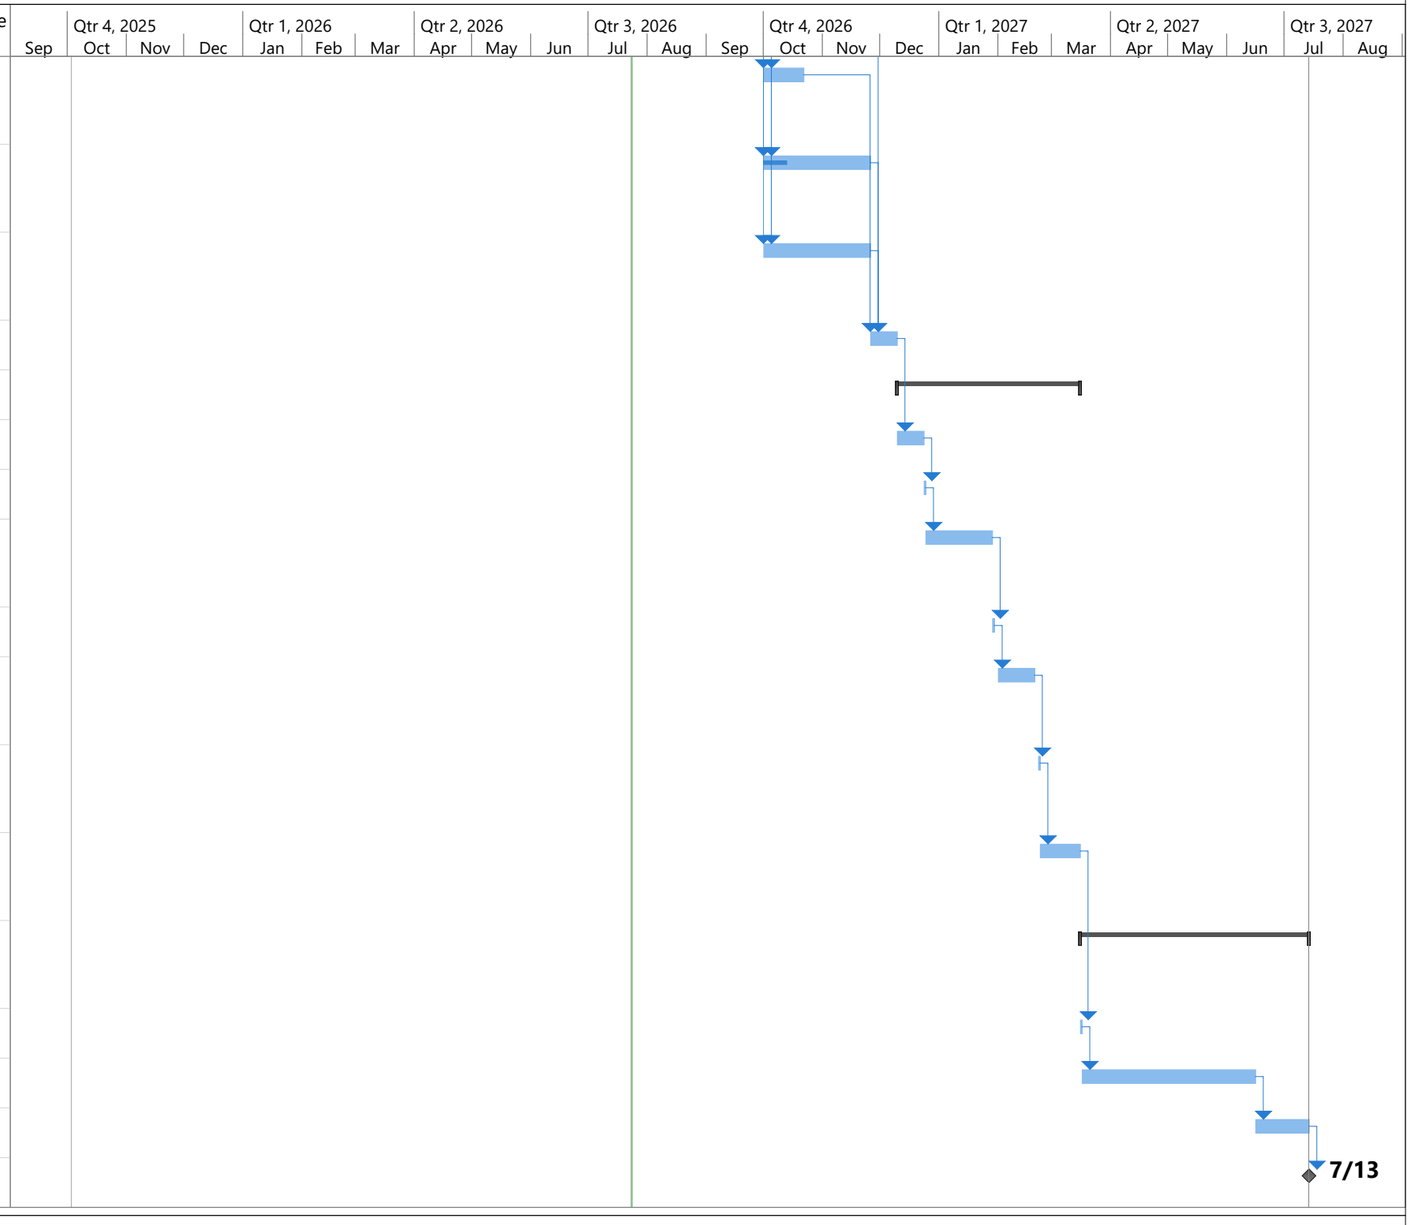

Project: 25.00136 FletcherNC-C
Date: Fri 7/24/26

Task	Project Summary	Manual Task	Start-only	Deadline
Split	Inactive Task	Duration-only	Finish-only	Progress
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress
Summary	Inactive Summary	Manual Summary	External Milestone
